

PROJECT DESCRIPTION  
GENERAL

THIS PORTION OF THE PROJECT INVOLVES THE OPERATION OF MOT PHASE 2 THE TEMPORARY TRAFFIC SIGNAL ON MD 35 OVER BRANCH OF WILLS CREEK BRIDGE REPLACEMENT LOCATED IN ALLEGANY COUNTY.

INTERSECTION OPERATION

NO CHANGE IN SIGNAL OPERATION REQUIRED IN THIS PHASE OF MOT 2. THE TRAFFIC SIGNAL EQUIPMENT SHALL BE REMOVED IN THIS PHASE.

SPECIAL NOTES

1. THE FOLLOWING CONTACT PERSONS FOR THIS PROJECT ARE AS FOLLOWS:

PROJECT CONTACTS:

MR. GEORGE H. SMALL, ASSISTANT DISTRICT ENGINEER - TRAFFIC  
PHONE: (301) 729-8444  
MR. JOHN TRUE, ASSISTANT DISTRICT ENGINEER - CONSTRUCTION  
PHONE: (301) 729-8411  
MR. ANTHONY CRAWFORD, ASSISTANT DISTRICT ENGINEER - MAINTENANCE  
PHONE: (301) 729-8457  
MR. ROBERT ROWAN, UTILITY ENGINEER  
PHONE: (301) 729-8439  
MR. RICHARD L. DAFF, SR. CHIEF TRAFFIC OPERATIONS DIVISION  
PHONE: (410) 787-7630

2. TEMPORARY TRAFFIC CONTROL TYPICAL APPLICATION STANDARD NO. MD 104.06-04 FOR ONE LANE ROAD (SIGNAL CONTROLLED) 2-LANE, 2-WAY FOR YOUR TRAFFIC CONTROL SIGNING.

EQUIPMENT LIST

A. EQUIPMENT TO BE SUPPLIED BY THE ADMINISTRATION.

CATEGORY CODE NO.	DESCRIPTION	UNITS	QUANTITY
	NONE		


B. EQUIPMENT TO BE FURNISHED AND/OR INSTALLED BY THE CONTRACTOR.

CATEGORY CODE NO.	DESCRIPTION	UNITS	QUANTITY
585624	24 IN. HEAT APPL. WHITE THERMO. PLASTIC PAVEMARKING	LF	20
585462	REMOVAL OF EXISTING PAVEMENT MARKINGS ANY WIDTH	LF	60
800000	REMOVE, SALVAGE, AND DISPOSE OF SIGNAL EQUIPMENT	LS	1
800000	RELOCATE EXISTING OVERHEAD SIGN	EA	2
800000	REALIGN EXISTING VIDEO CAMERA	EA	1
860265	RELOCATE EXISTING SIGNAL HEAD	EA	4

C. SHA FORCES SHALL REMOVE THE CONTROLLER AND ALL AUXILIARY EQUIPMENT FROM THE CONTROLLER CABINET. THE CABINET AND ALL OTHER MATERIALS TO BE REMOVED BY THE CONTRACTOR SHALL BECOME THE PROPERTY OF THE CONTRACTOR EXCEPT FOR THE FOLLOWING:

CATEGORY CODE NO.	DESCRIPTION	UNITS	QUANTITY
	CONTROLLER	EA	1
	STEEL SIGNAL STRUCTURE MAST ARM POLE WITH 40 FT ARM	EA	1
	STEEL SIGNAL STRUCTURE MAST ARM POLE WITH TWIN 50 FT ARMS	EA	1

WIRING DIAGRAM

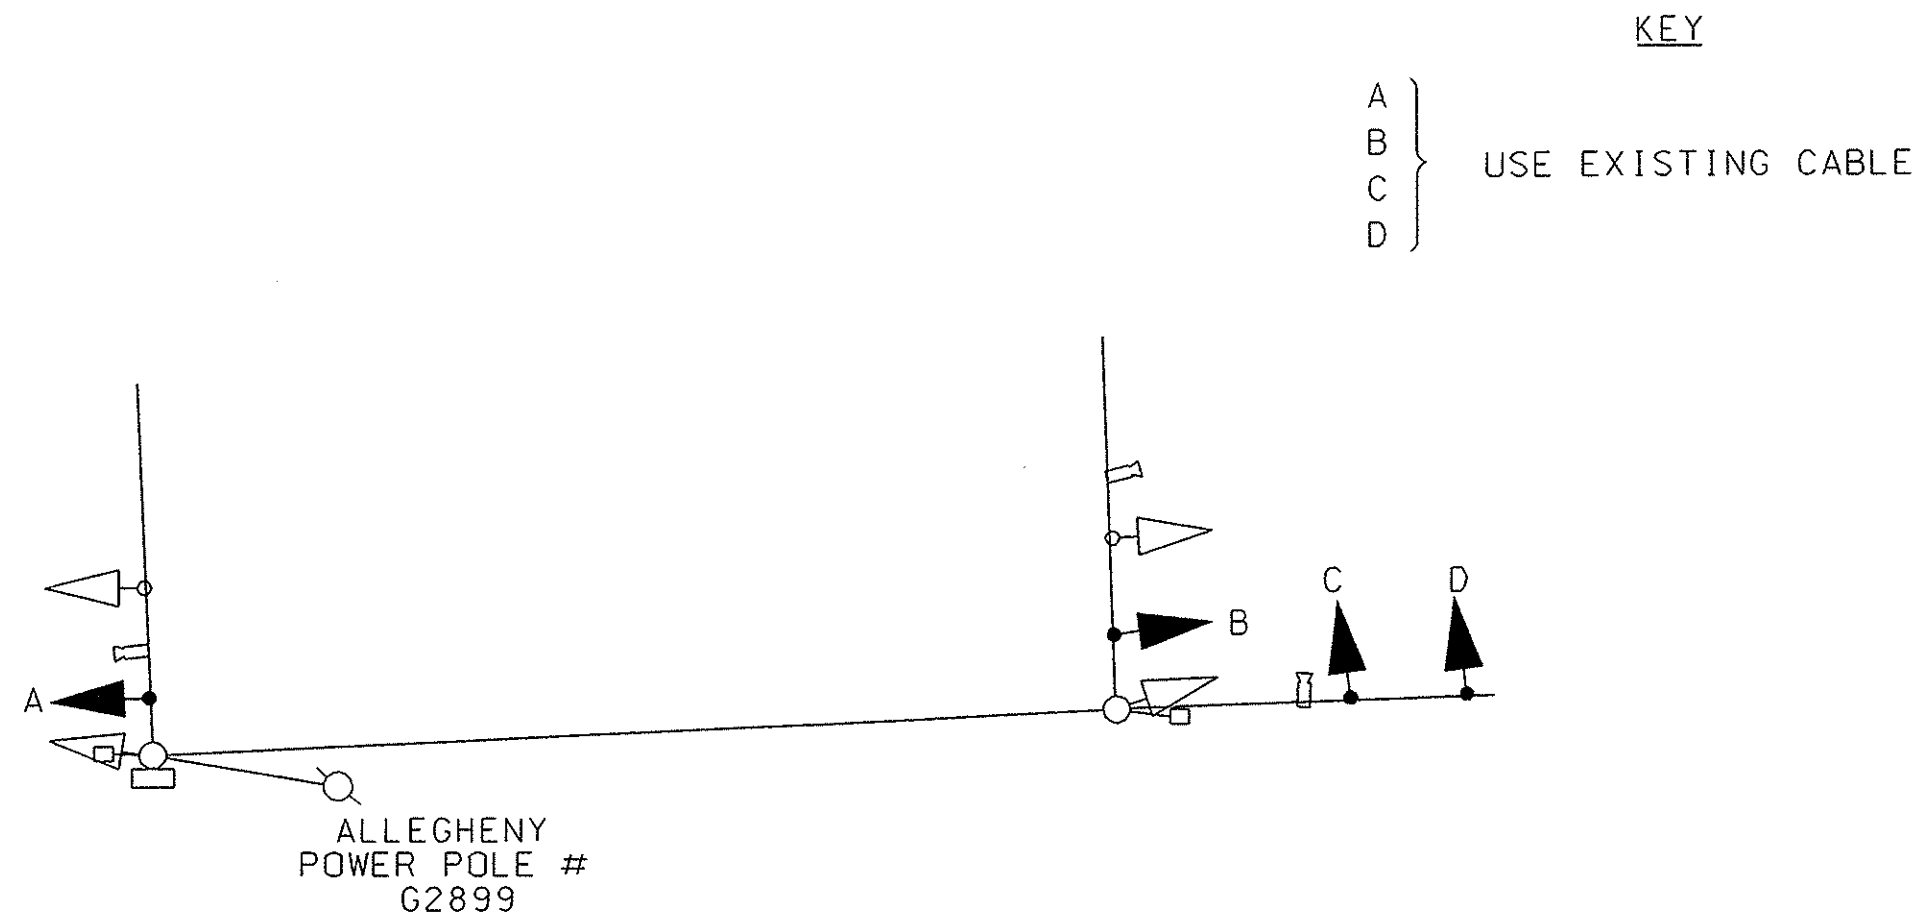

PHASE CHART

NO CHANGE HAS BEEN MADE  
IN THIS PHASE



STATE OF MARYLAND  
DEPARTMENT OF TRANSPORTATION  
STATE HIGHWAY ADMINISTRATION  
OFFICE OF TRAFFIC & SAFETY  
TRAFFIC ENGINEERING DESIGN DIVISION

MD 35 OVER BRANCH OF WILLS CREEK  
BRIDGE NO. 01068 REPLACEMENT

ELLERSLIE, MARYLAND

MOT (PHASE 2) TEMPORARY TRAFFIC SIGNAL GENERAL INFORMATION PLAN

SCALE NONE DATE FEBRUARY 2007 CONTRACT NO. AL6205180

DESIGNED BY S. SMITH COUNTY ALLEGANY  
DRAWN BY S. SMITH LOGMILE 010036002.16 TO 010036002.24  
CHECKED BY J. WEAVER TMS NO. H136  
FAP NO. TOD NO.

TS NO. 4450 DRAWING PSG OF N002 SHEET NO. 12 OF 66

SABRA, WANG & ASSOCIATES, INC.  
1504 JOH AVENUE  
SUITE 160  
BALTIMORE, MD 21227  
(410) 737-6564  
WWW.SABRA-WANG.COM
